

- *CIVIL WORKS IN OPD BLOCK*
- *CIVIL WORKS IN IPD BLOCK*
- *PROJECT WEEKLY ACTIVITIES*
- *FINANCIAL DETAILS*
- *PICTURE EXCERPTS*

STELLA OBASANJO HOSPITAL

Edo state ministry of Health

**PROGRESS REPORT: WEEK 7
(13th – 18th February 2023)**

Civil works in OPD block


% PERCENTAGE COMPLETION

14, February 2023

45.8%

ONGOING WEEK 7 ACTIVITIES

Plastering of internal & external walls	70%
Casting of parapet wall	100%
MEPF first fix	61.25%
Primer painting	12.50%
Hydrotherapy pool pump house wall	5%

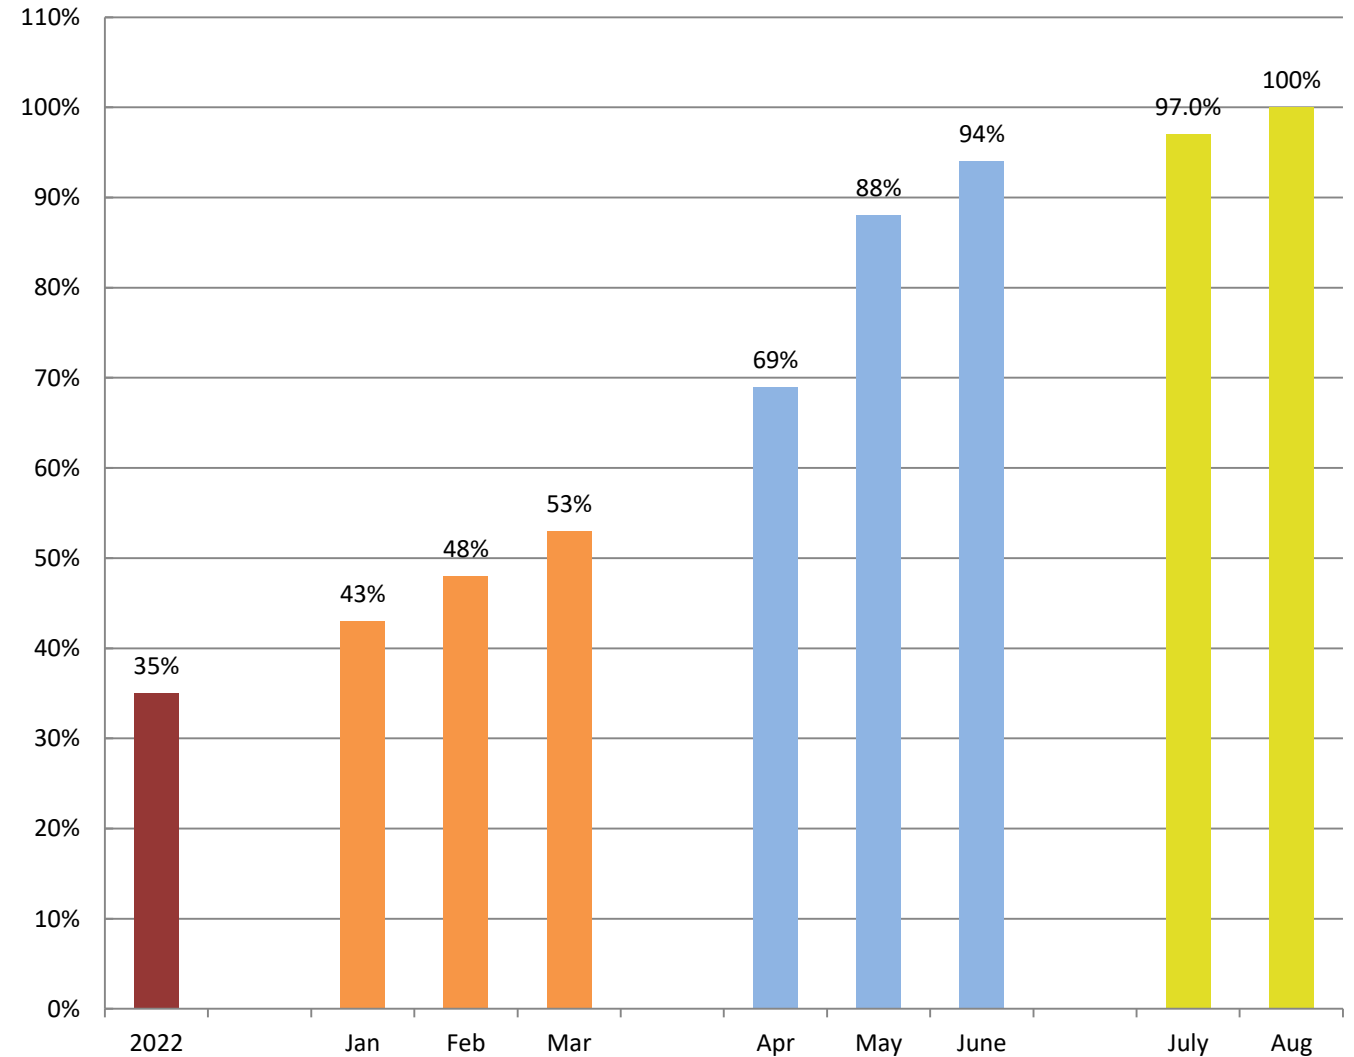

Civil works in IPD block

% PERCENTAGE COMPLETION

09, February 2023

0.75%


ONGOING ACTIVITIES

- NIL

PREVIOUS ACTIVITIES IN IPD

- Removal of suspended ceiling
- Removal of sanitary wares
- Removal Air-conditioners

All item carefully accounted for and stored in container on site

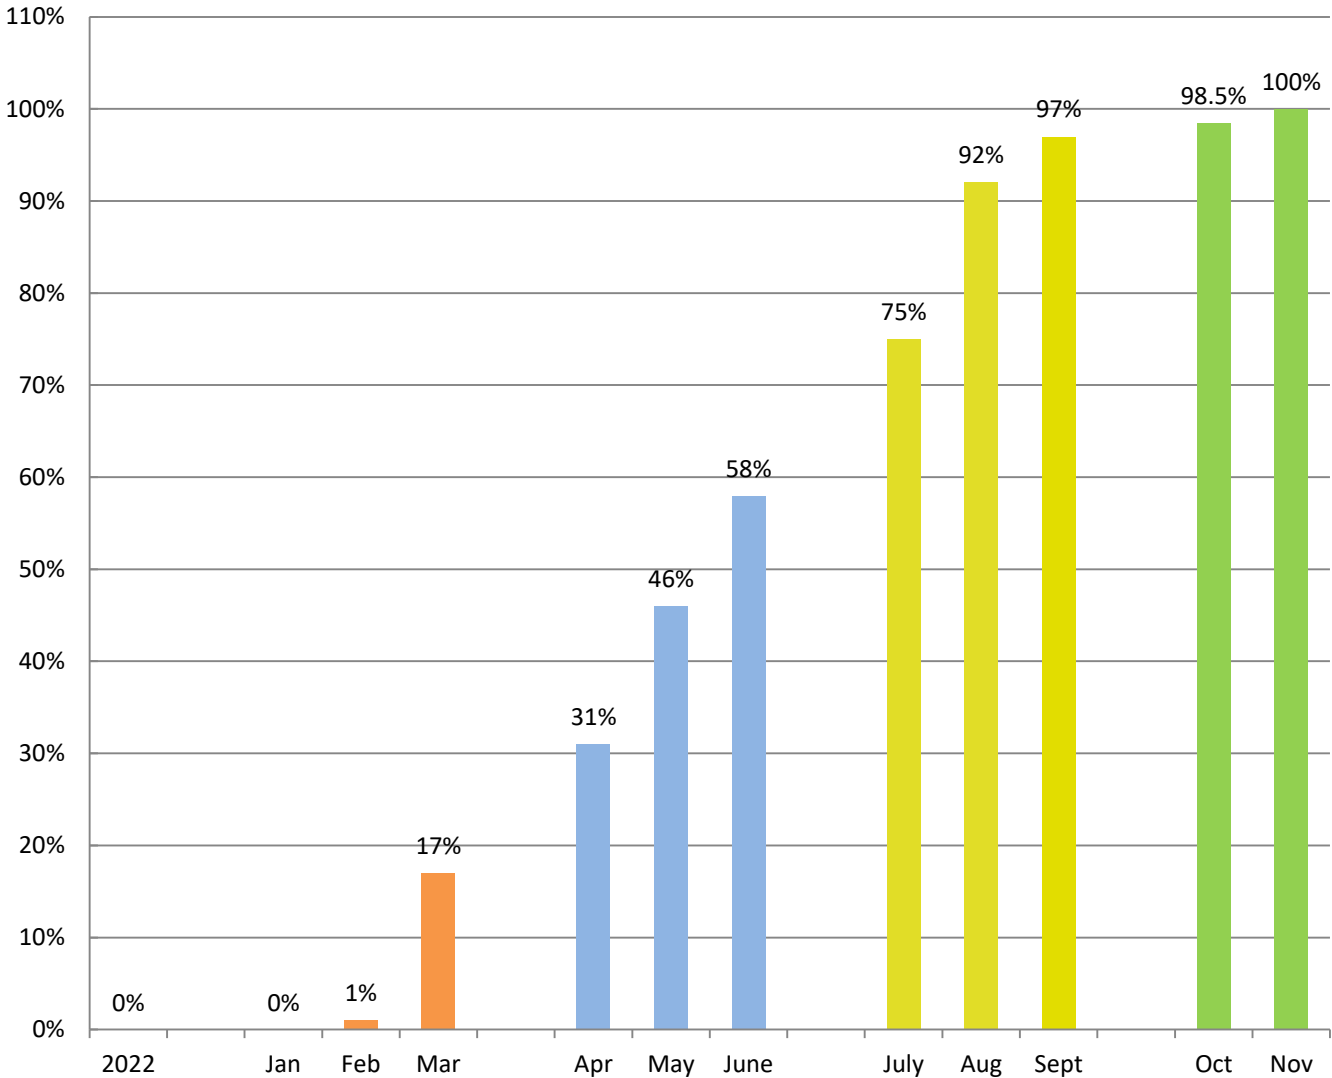

Project weekly activities

WEEK 7: 13th – 18th February, 2023

TASK/ACTIVITY				% EXPECTED CUMULATIVE TARGET (OPD & IPD)
OPD		IPD		
Activity	% Expected Cumulative weekly target	Activity	% Expected Cumulative weekly target	
<ul style="list-style-type: none">Internal & External plastering works	46.75	Financial options payment and cash flow plan being processed	0.75	24.25
<ul style="list-style-type: none">General MEPF first fix				
<ul style="list-style-type: none">Block work in hydrotherapy pool pump house				
<ul style="list-style-type: none">Primer painting				

In view : WEEK 8

TASK/ACTIVITY				% EXPECTED CUMULATIVE TARGET (OPD & IPD)
OPD		IPD		
Activity	% Expected Cumulative weekly target	Activity	% Expected Cumulative weekly target	
• Internal & External plastering works	48	Financial options payment and cash flow plan being processed	1	
• General MEPF first fix				
• Block work in hydrotherapy pool pump house				
• Primer painting				

Financial Details

ACTIVITY	STATUS
OPD CIVIL WORKS	Interim valuation certificate for OPD Civil works currently been processed by MOH
IPD CIVIL WORKS	Contractor awaiting mobilization
MEDICAL & NON-MEDICAL EQUIPMENTS	Invoices received from vendors. Financial options payment and cash flow plan being processed Vendors awaiting mobilization

Picture excerpts



Electrical piping works in OPD



Perspective view of external plaster works in OPD

Picture excerpts



Primer painting works in OPD



Hydrotherapy pull pump house


Picture excerpts



Front view perspective of IPD



Careful removal of suspended ceiling in IPD



Let love lead ❤️
